

Inspection Marks

Locate Compression Ring Here

Cut Pipe Here

# CUTTING TEMPLATE

Securely hold or tape this Cutting Template to the desired Cell Vessel installation location. Use a waterproof permanent marker to mark the pipe. When finished, there should be 12 marks on the pipe. Follow procedures on the Installation Quick Start Guide to complete Vessel installation.

Inspection Marks

Locate Compression Ring Here

Cut Pipe Here


Use to mount \_\_\_\_\_ on post

Use to mount \_\_\_\_\_ on flat surface


# MOUNTING TEMPLATE

Use the included hardware or your own hardware (suitable for a 20lb load) to mount the Control Box to a wall or post within 3 feet of a GFCI outlet, making sure that the cord will reach. Use this template to locate and drill fastener holes.

Secure Mounting Template to desired mounting location and drill mounting holes.




1




Screw in top fasteners leaving 1/8" space between screw head and surface

2




Hang Control Box on fasteners

3

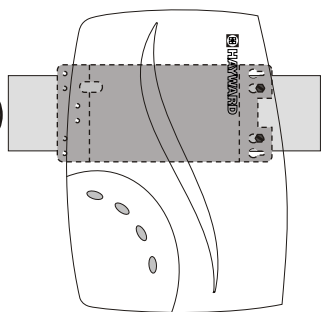

Screw in bottom fasteners securely.

4

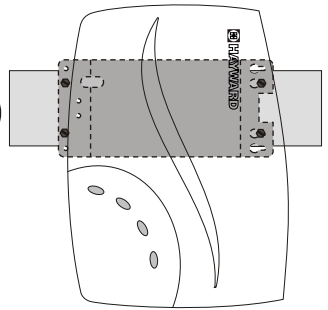

Use to mount \_\_\_\_\_ on flat surface

Use to mount \_\_\_\_\_ on post
